Activity ID	Activity Name	Rem Dur	Deerfield Town	Expected Start	Expected Finish
T1023C	**Deerfield S/S Auto XFMR & 345kV -...**	563d		05-Oct-09	30-Nov-11
1649	Install 345 kV Circuit Switcher Foundation	5d	Town	05-Oct-09	09-Oct-09
1961	Receive 345kV CCVT's (lead time)	70d	Town	07-Oct-09	20-Jan-10
1987	Receive 345kV Slip On CT's (Lead Time)	60d	Town	07-Oct-09	06-Jan-10
1652	Install 115 kV Switch Foundation	5d	Town	13-Oct-09	19-Oct-09
1597	Install 345kV Breaker Slabs	5d	Town	13-Oct-09	19-Oct-09
1728	XFMR Initial Testing (Bushings, CT, & Core Insul) & Accessory P...	3d	Town	15-Oct-09	17-Oct-09
1729	Assemble XFMR Coservator, Radiators, Bushings & Pipe Asmbly	7d	Town	18-Oct-09	24-Oct-09
1596	Install Remaining 345kV Bus Support Foundations	5d	Town	20-Oct-09	26-Oct-09
1766	Backfill Oil Containment System	3d	Town	20-Oct-09	22-Oct-09
1647	Install Remaining 115 kV Bus Support Foundations	5d	Town	20-Oct-09	26-Oct-09
1734	Install Drops to XFMR	3d	Town	25-Oct-09	27-Oct-09
1738	XFMR Oil Tank Discharge & Preparation	5d	Town	25-Oct-09	29-Oct-09
1147	Survey Road Conditions After Heavy Equipment Deliveries	5d	Town	27-Oct-09	02-Nov-09
1767	Hutter Final Cleanup & Demobilization	3d	Town	27-Oct-09	29-Oct-09
1153	Town Of Deerfield Repair Culvert (Town Maintenance)	2d	Town	27-Oct-09	28-Oct-09
1598	Install Remaiing 345kV Bus Support Foundations	5d	Town	27-Oct-09	02-Nov-09
1739	XFMR Oil Treatment, Leakage Test, Vacuum, Oil Filling, & Circul...	9d	Town	30-Oct-09	07-Nov-09
1148	Grind & Grade Cate Road	8d	Town	03-Nov-09	13-Nov-09
1744	Deliver & Off Load 1st & 2nd Oil Tankers	1d	Town	03-Nov-09	03-Nov-09
1745	Deliver & Off Load 3rd & 4th Oil Tankers	1d	Town	04-Nov-09	04-Nov-09
1651	Receive 345 kv (3) Breakers (ETA - 11-05-09)	1d	Town	05-Nov-09*	05-Nov-09
1746	Deliver & Off Load 5th & 6th Oil Tankers	1d	Town	05-Nov-09	05-Nov-09
1747	XFMR Electrical Assembly & Preliminary Tests	5d	Town	08-Nov-09	12-Nov-09
1741	Receive 345 Circuit Switches (2) (ETA 11-13-09)	1d	Town	13-Nov-09*	13-Nov-09
1783	Receive 345kV MOABs (2) (ETA 11-13-09)	1d	Town	13-Nov-09*	13-Nov-09
1784	Receive 345kV Circuit Switches Stand (1) (ETA 11-13-09)	1d	Town	13-Nov-09*	13-Nov-09
1971	Receive Static Masts (lead time)	30d	Town	16-Nov-09	30-Dec-09
1149	Pave Cate Road	2d	Town	16-Nov-09	17-Nov-09
1610	Receive Support Steel (lead time)	40d	Town	19-Nov-09	19-Jan-10
1644	Receive Connectors (lead time)	30d	Town	23-Nov-09	07-Jan-10
1668	Receive Bus Material (lead time)	40d	Town	23-Nov-09	21-Jan-10
1965	Receive 345kV Station Post Insulators (lead time)	40d	Town	23-Nov-09	21-Jan-10

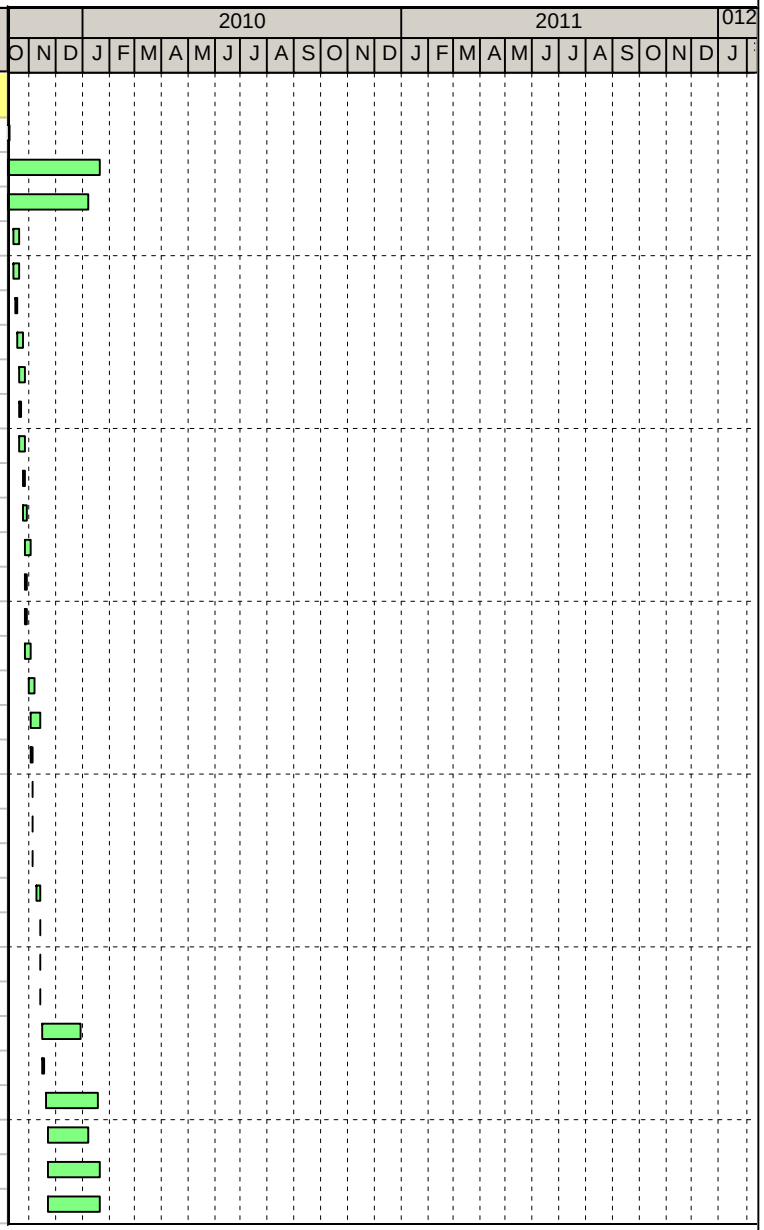

Deerfield S/S Auto Transformer

Preliminary Schedule

Run Date: 09-Oct-09 09:1

Data Date: 05-Oct-09
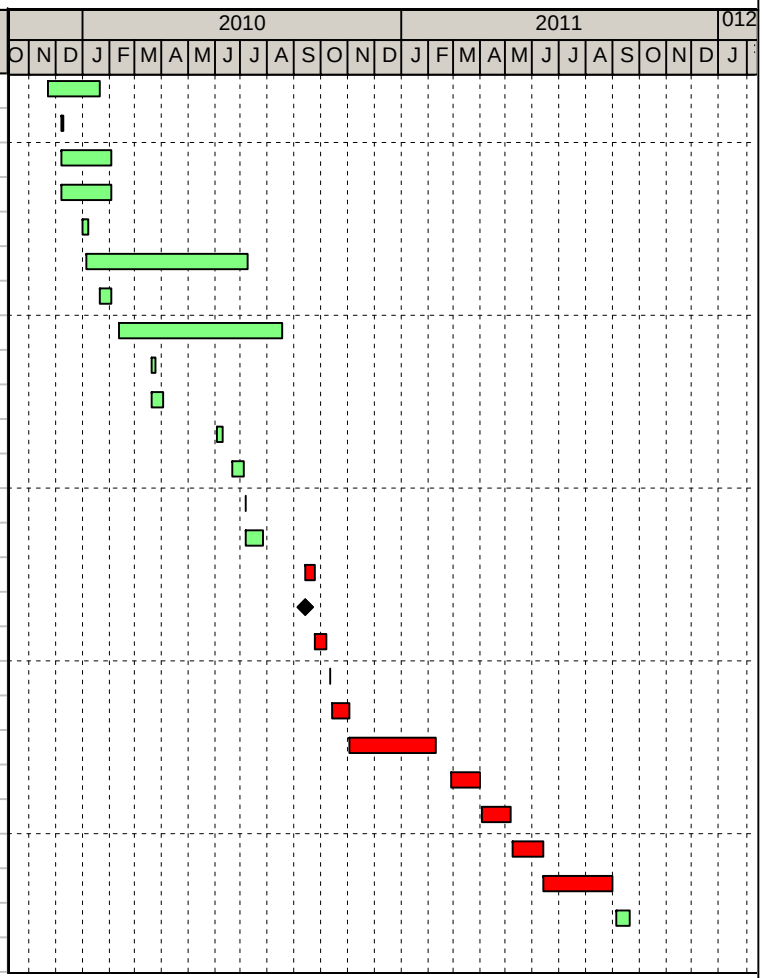
Activity ID	Activity Name	Rem Dur	Deerfield Town	Expected Start	Expected Finish
8886	Receive Ground Wire (lead time)	40d	Town	23-Nov-09	21-Jan-10
1707	Install Xfmr Foundation Cable Trench (Pad To Control Bldg)	3d	Town	08-Dec-09	10-Dec-09
1703	Install Cable Trench	40d	Town	08-Dec-09	03-Feb-10
1704	Repair Existing Cable Trenches	40d	Town	08-Dec-09	03-Feb-10
1840	Assemble / Issue Elec/Civil Construction Pkg - Above Grade	5d	Town	31-Dec-09	07-Jan-10
4045	Receive Automated Transfer Switch (Lead Time)	130d	Town	05-Jan-10	08-Jul-10
1768	Install Support Steel	10d	Town	20-Jan-10	02-Feb-10
1505	Receive Backup Generator (Lead Time)	130d	Town	12-Feb-10	17-Aug-10
1968	Install 345kV CCVT's	4d	Town	22-Mar-10	25-Mar-10
1769	Install 115kV Bus Expansion	10d	Town	22-Mar-10	02-Apr-10
4230	Assemble + Issue P/C Drawing Package - IFC	5d	Town	03-Jun-10	10-Jun-10
4249	Receive Control Cabinets (Lead Time)	10d	Town	22-Jun-10	05-Jul-10
1964	Issue 345kV Breaker DX Switches To Project (In Stock)	1d	Town	06-Jul-10*	06-Jul-10
1654	Install 345 DX Switches (2)	15d	Town	07-Jul-10	27-Jul-10
4054	Construct Backup Generator Foundation & Conduit	10d	Town	13-Sep-10	24-Sep-10
1537	Construction Start - Backup Generator Installation	0d	Town	13-Sep-10*	
4063	Backup Generator Foundation Cure Time	14d	Town	25-Sep-10	08-Oct-10
4053	Place Backup Generator on Foundation	1d	Town	12-Oct-10	12-Oct-10
4065	Commission Backup Generator	15d	Town	13-Oct-10	02-Nov-10
1780	Install Cable Tray Conductor & Perform Field Terminations	100d	Town	03-Nov-10	10-Feb-11
1779	Install 1st 345kV Breaker Relay Upgrades	25d	Town	28-Feb-11*	01-Apr-11
1778	Install 2nd 345kV Breaker Relay Upgrades	25d	Town	04-Apr-11	06-May-11
1765	Install 3rd 345kV Breaker Relay Upgrades	25d	Town	09-May-11	13-Jun-11
1777	Control House 345kV P&C Upgrades & BPS	80d	Town	14-Jun-11	01-Sep-11
5046	Replace Ciruit Switch TB14	15d	Town	05-Sep-11*	19-Sep-11
7595	Deerfield Battery Replacement	59d	Town	03-Oct-11	30-Nov-11
